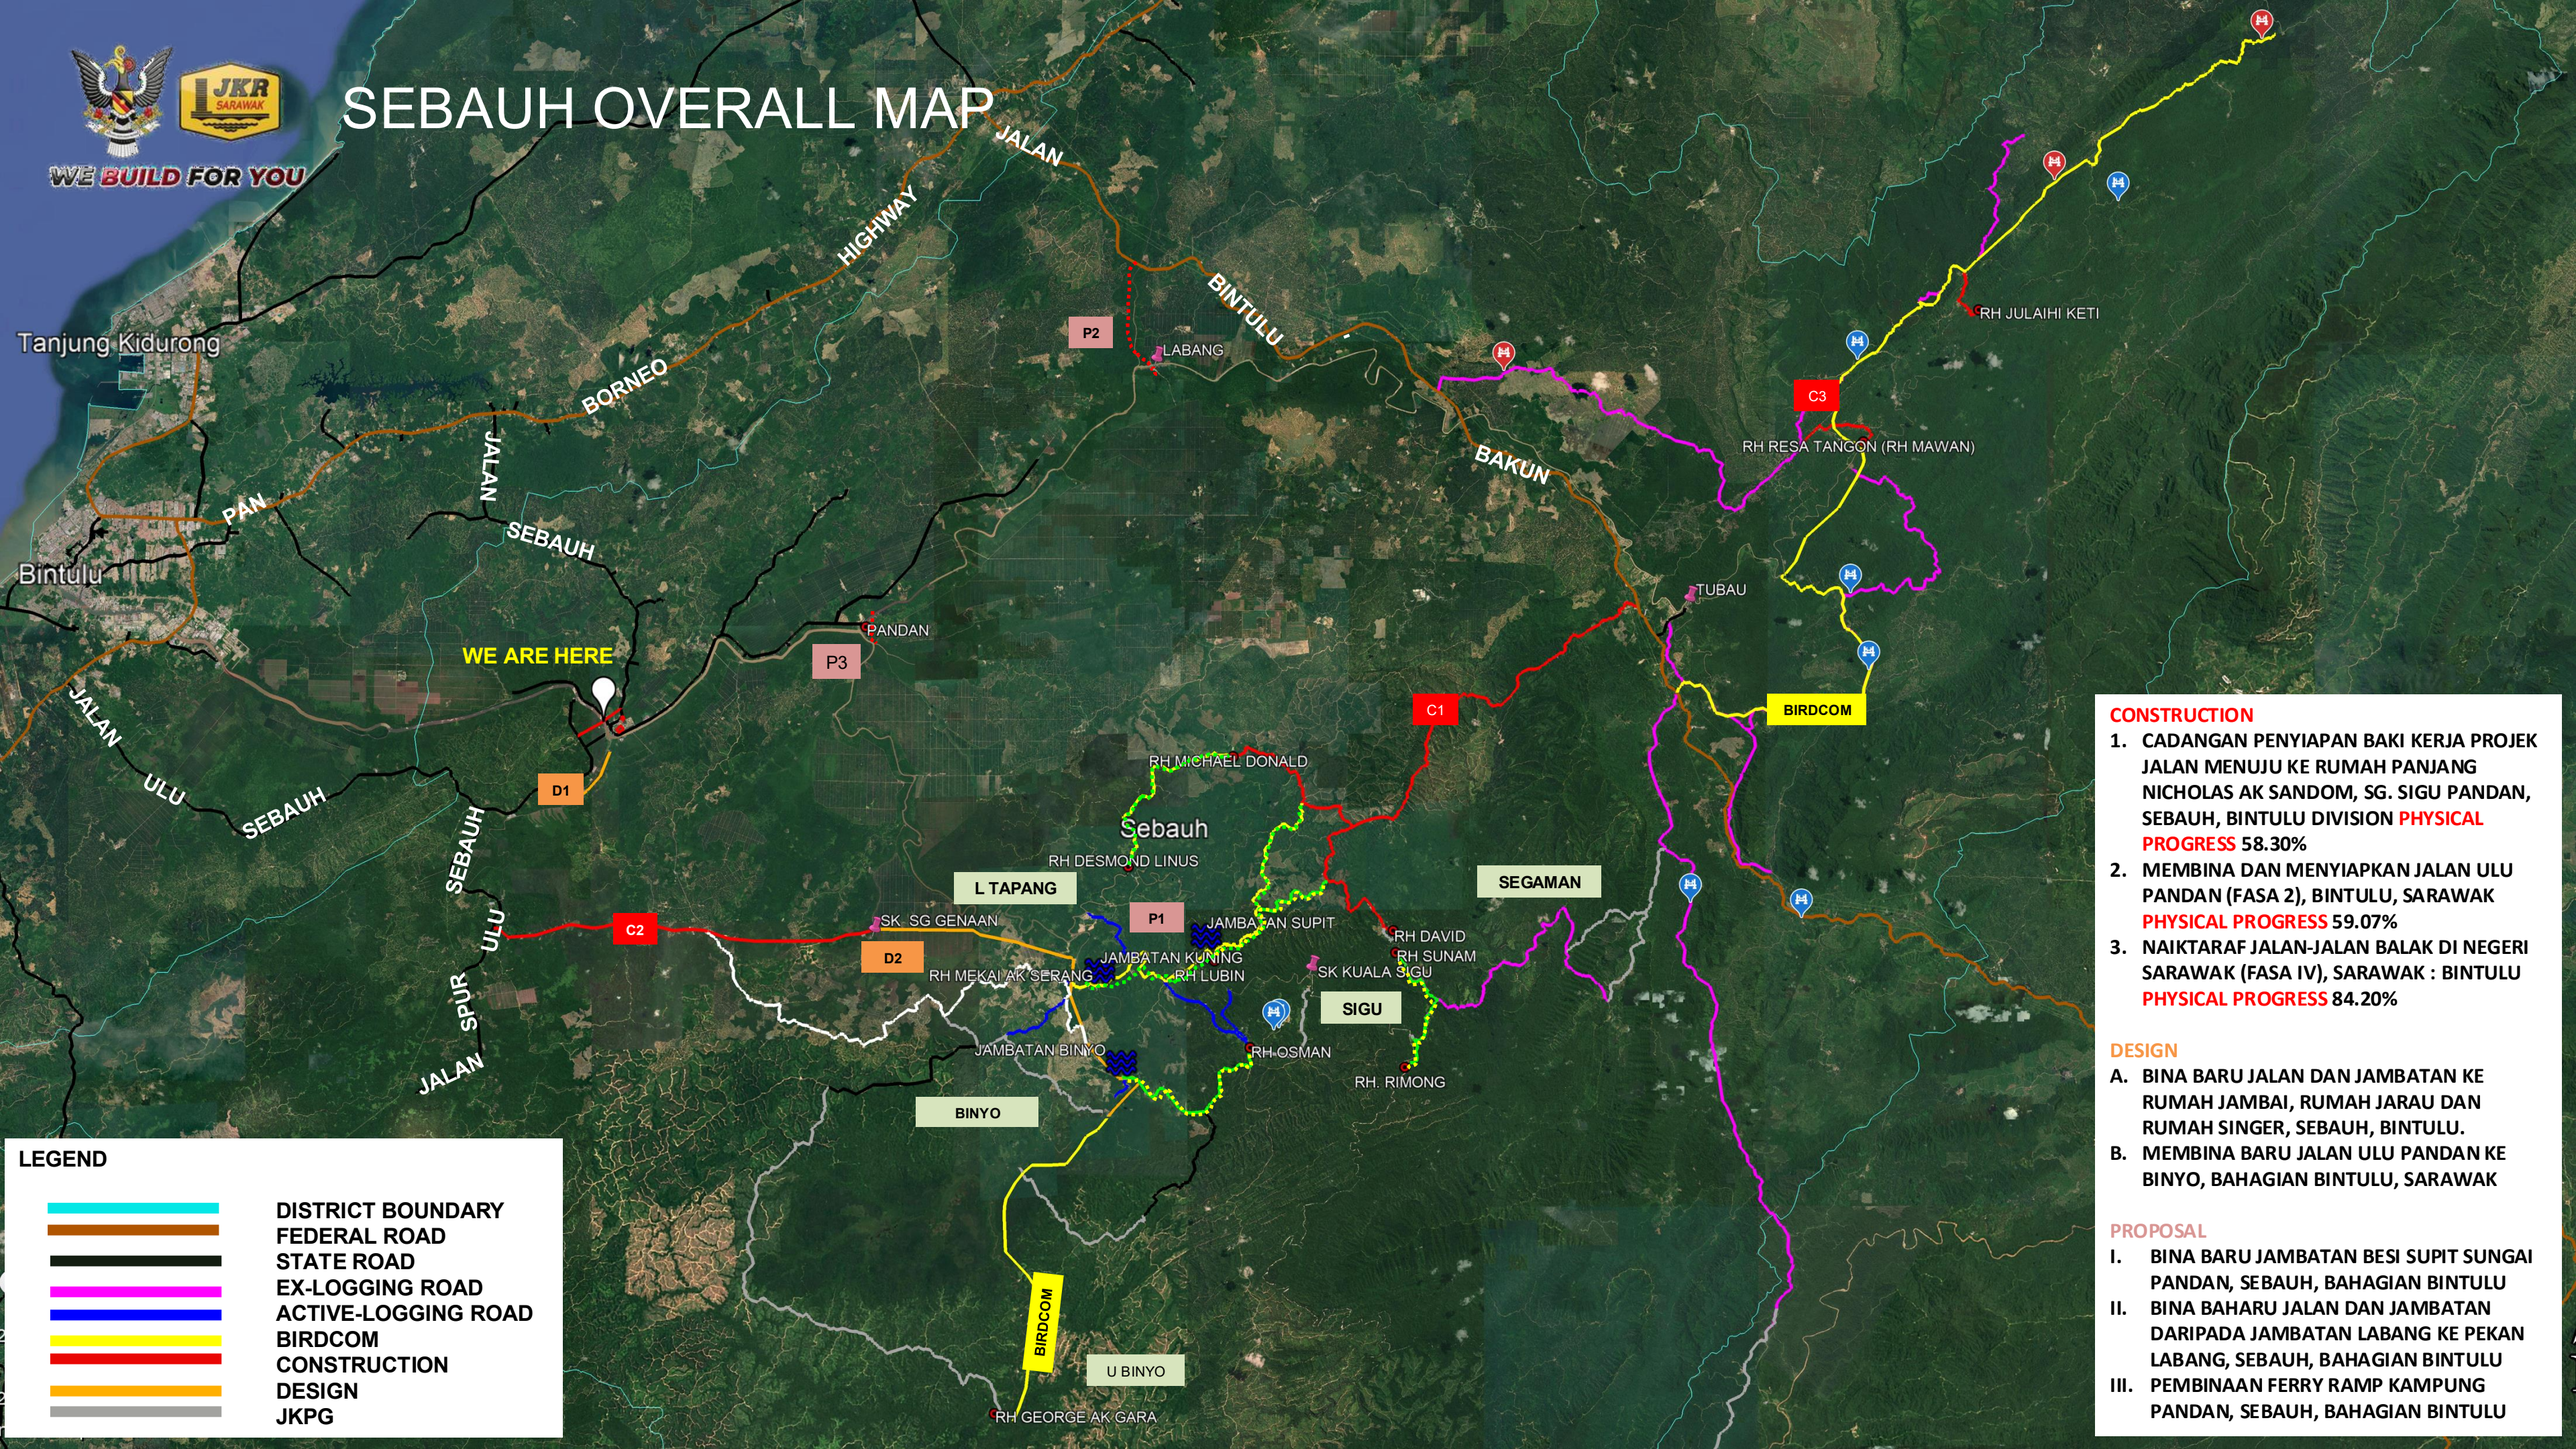


LEGEND

- DISTRICT BOUNDARY
- FEDERAL ROAD
- STATE ROAD
- EX-LOGGING ROAD
- ACTIVE-LOGGING ROAD
- BIRDCOM
- CONSTRUCTION
- DESIGN
- JKPG

CONSTRUCTION

1. CADANGAN PENYIAPAN BAKI KERJA PROJEK JALAN MENUJU KE RUMAH PANJANG NICHOLAS AK SANDOM, SG. SIGU PANDAN, SEBAUH, BINTULU DIVISION PHYSICAL PROGRESS 58.30%
2. MEMBINA DAN MENYIAPKAN JALAN ULU PANDAN (FASA 2), BINTULU, SARAWAK PHYSICAL PROGRESS 59.07%
3. NAIKTARAF JALAN-JALAN BALAK DI NEGERI SARAWAK (FASA IV), SARAWAK : BINTULU PHYSICAL PROGRESS 84.20%

DESIGN

A. BINA BARU JALAN DAN JAMBATAN KE RUMAH JAMBAI, RUMAH JARAU DAN RUMAH SINGER, SEBAUH, BINTULU.
B. MEMBINA BARU JALAN ULU PANDAN KE BINYO, BAHAGIAN BINTULU, SARAWAK

PROPOSAL

I. BINA BARU JAMBATAN BESI SUPIT SUNGAI PANDAN, SEBAUH, BAHAGIAN BINTULU
II. BINA BAHARU JALAN DAN JAMBATAN DARIPADA JAMBATAN LABANG KE PEKAN LABANG, SEBAUH, BAHAGIAN BINTULU
III. PEMBINAAN FERRY RAMP KAMPUNG PANDAN, SEBAUH, BAHAGIAN BINTULU

CONSTRUCTION

CADANGAN PENYIAPAN BAKI KERJA PROJEK JALAN MENUJU KE RUMAH PANJANG NICHOLAS AK SANDOM, SG. SIGU PANDAN, SEBAUH, BINTULU DIVISION

PROJECT TITLE	CADANGAN PENYIAPAN BAKI KERJA PROJEK JALAN MENUJU KE RUMAH PANJANG NICHOLAS AK SANDOM, SG. SIGU PANDAN, SEBAUH, BINTULU DIVISION
SCOPE OF WORK	A) CONSTRUCTION OF 40.7KM ROAD B) CONSTRUCITON OF 3 NEW BRIDGES C) CONSTRUCTION OF CULVERT D) CONSTRUCTION OF DRAINAGE E) EARTHWORK F) PAVEMENT G) ROAD FURNITURE H)ELECTRIC POLE RELOCATION
CONTRACT PERIOD	START DATE : 31/01/2025 COMPLETION DATE : 30/01/2028
COST PROJECT	RM 207,394,222.94
PHYSICAL PROGRESS	58.30%









CONSTRUCTION

MEMBINA DAN MENYIAPKAN JALAN ULU PANDAN (FASA 2), BINTULU, SARAWAK

PROJECT TITLE	MEMBINA DAN MENYIAPKAN JALAN ULU PANDAN (FASA 2), BINTULU, SARAWAK
SCOPE OF WORK	1. NEW TAR-SEALED ROAD (A) 8KM OF JKR R3 ROAD – MAIN ROAD (B) 6KM OF JKR R1 ROAD – SPUR ROAD 2. RECTIFICATION WORKS TO 11KM JALAN ULU PANDAN PHASE 1 3. R.C BRIDGES A) SG SEBAUH - 60M B) SG GENAAN – 30M 4.COMPLETION OF CULVERTS, DRAINAGES, SLOPE PROTECTION AND ROAD SHOULDERS. 5. INSTALLATION OF ROAD FURNITURE.
CONTRACT PERIOD	START DATE : 13/01/2022 COMPLETION DATE : 29.09.2027 (EOT NO.9)
COST PROJECT	RM 96,049,259.00
PHYSICAL PROGRESS	59.07%





CONSTRUCTION

NAIKTARAF JALAN-JALAN BALAK DI NEGERI SARAWAK (FASA IV): BINTULU

PROJECT TITLE	NAIKTARAF JALAN-JALAN BALAK DI NEGERI SARAWAK (FASA IV): BINTULU
SCOPE OF WORK	A) SITE CLEARING AND EARTHWORKS B) DEVELOPING AND UPGRADING OF EXISTING 7.256 KM EARTH ROAD TO JKR R1 C) DRAINAGES AND CULVERTS WORKS D) ROAD FURNITURE AND ENVIRONMENTAL PROTECTION WORKS
CONTRACT PERIOD	START DATE : 09/05/2025 COMPLETION DATE : 19/02/2027 (EOT NO.2)
COST PROJECT	RM 22,099,695.78
PHYSICAL PROGRESS	84.20%











DESIGN


BINA BARU JALAN DAN JAMBATAN KE RUMAH JAMBAI, RUMAH JARAU DAN RUMAH SINGER, SEBAUH, BINTULU.

ITEM	DESCRIPTION
SCOPE OF WORK	1) R1 MODIFIED GRAVEL ROAD : 1.5KM 2) STEEL BRIDGE : 90M (L) X 5M (W) (SINGLE LANE ONLY)
APPROVED CEILING COST (RM)	RM 27,000,000.00

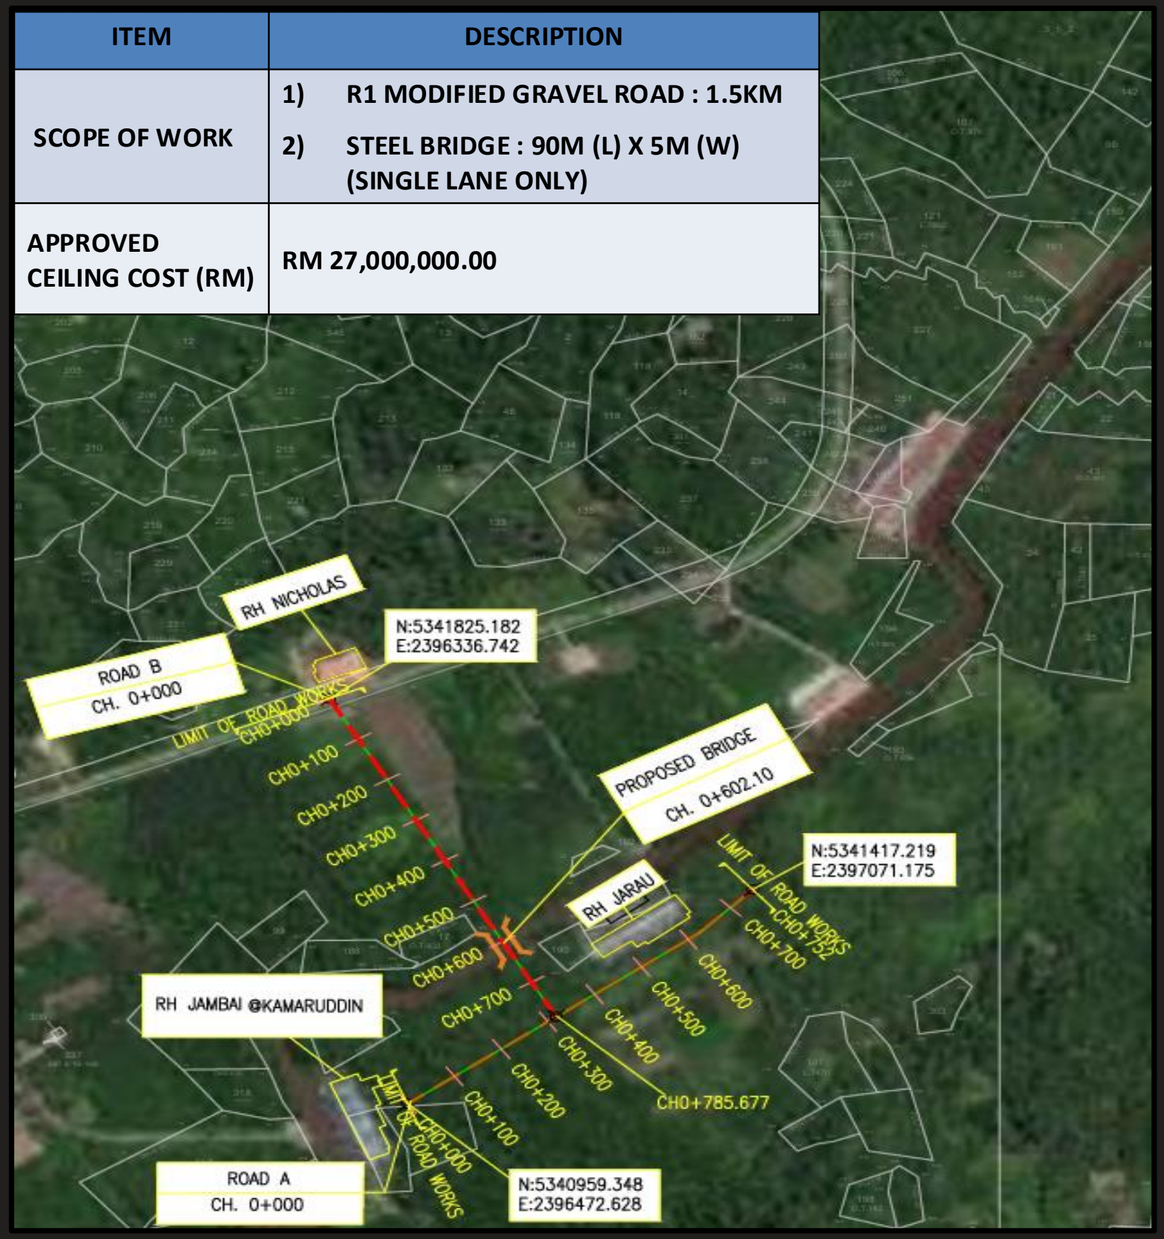

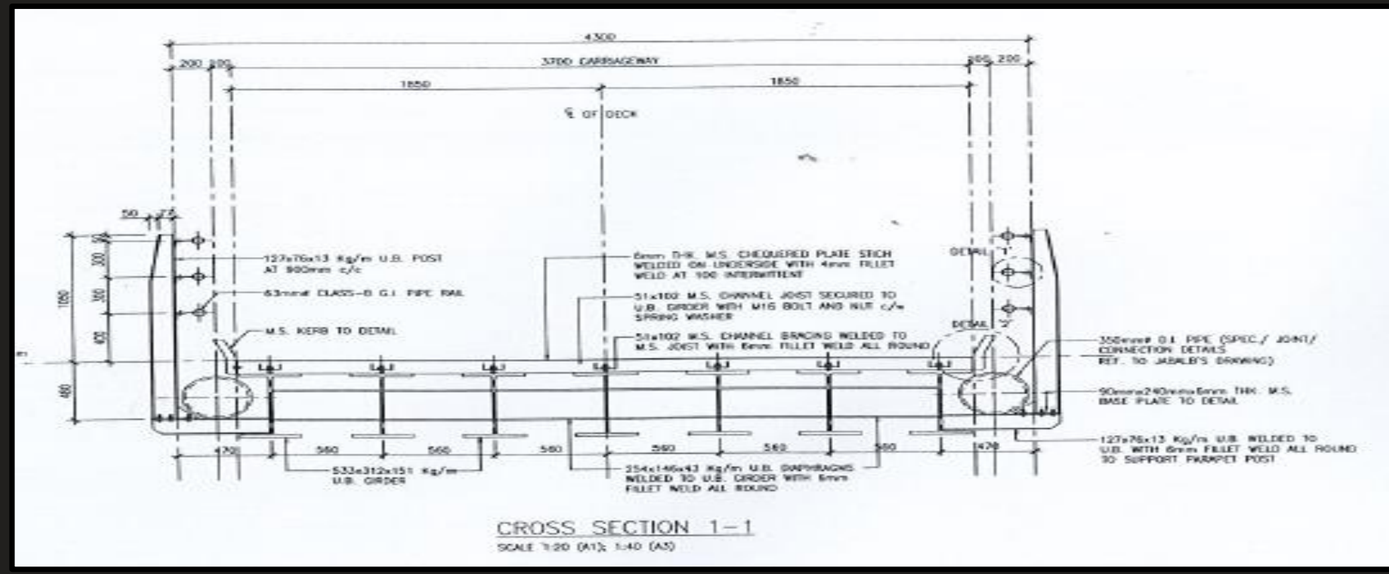

Typical Single Lane Bridge Cross Section

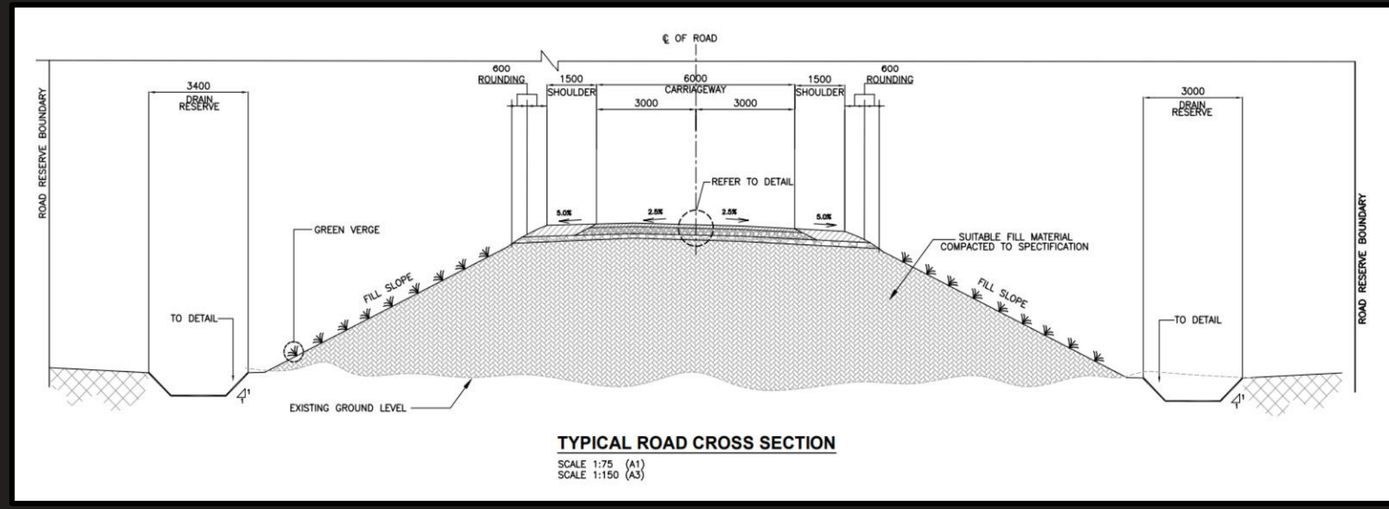

Typical Single Lane Bridge Cross Section

DESIGN

BINA BARU JALAN DAN JAMBATAN KE RUMAH JAMBAI, RUMAH JARAU DAN RUMAH SINGER, SEBAUH, BINTULU.


PHASE 1

SCOPE OF WORK : 1) R1 MODIFIED GRAVEL ROAD : 1.5KM

2) STEEL BRIDGE : 90M (L) X 5M (W)

(SINGLE LANE ONLY)

APPROVED CEILING COST: RM 27,000,000.00

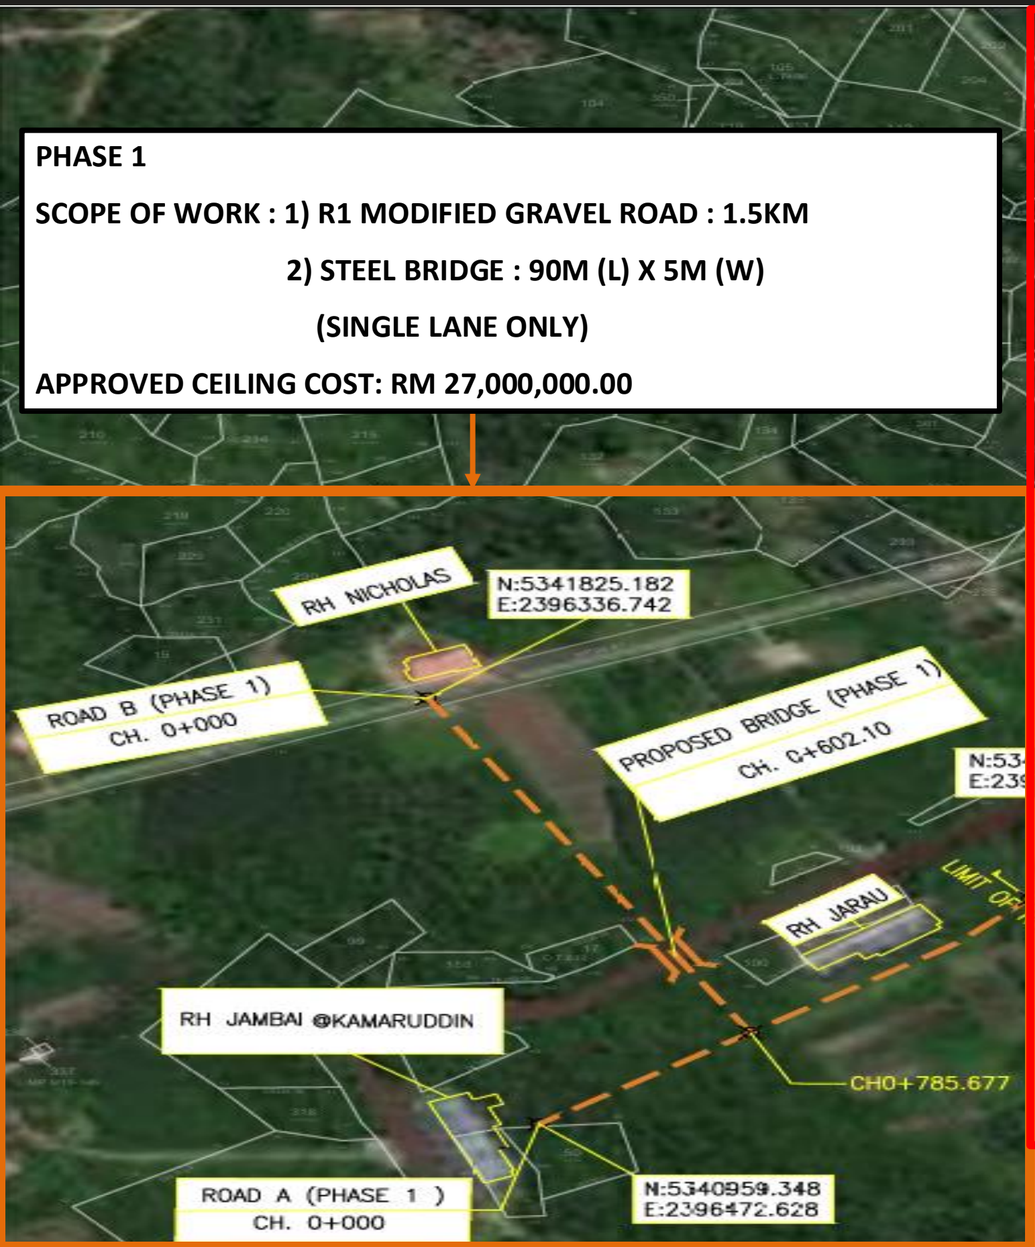



PHASE 2

SCOPE OF WORK :

1) R1 MODIFIED ROAD : 2KM

2) HDPE PIPE CULVERT : 4 NOS

DESIGN

MEMBINA BARU JALAN ULU PANDAN KE BINYO,BAHAGIAN BINTULU, SARAWAK.

ITEM	DESCRIPTION
SCOPE OF WORK	1) PAVED ROAD (R1) = 15KM 2) GRAVEL ROAD (R1) = 1.5KM
APPROVED CEILING COST (RM)	RM 120,000,000.00

